City of Commerce City - 2026 Mill & Overlay

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		**Base Bid + Alternates**	**43 days**	**Mon 7/6/26**	**Wed 9/2/26**		
2		**Area 3**	**8 days**	**Mon 7/6/26**	**Wed 7/15/26**		
3		Milling (12,124 SY)	1 day	Mon 7/6/26	Mon 7/6/26		
4		Patching	1 day	Tue 7/7/26	Tue 7/7/26	3	
5		Paving (1,031 Tons)	2 days	Wed 7/8/26	Thu 7/9/26	3,4	
6		Install Speed Humps	2 days	Fri 7/10/26	Mon 7/13/26	5	
7		Install Pavement Markings	2 days	Tue 7/14/26	Wed 7/15/26	6	
8		**Area 1**	**11 days**	**Tue 7/7/26**	**Tue 7/21/26**		
9		1.5" Milling (35,600 SY)	4 days	Tue 7/7/26	Fri 7/10/26	3	
10		Full Depth Patch	1 day	Fri 7/10/26	Fri 7/10/26	9FS-1 day	
11		1.5" Paving (3,028 Tons)	4 days	Mon 7/13/26	Thu 7/16/26	5,9,10	
12		Install Pavement Markings	3 days	Fri 7/17/26	Tue 7/21/26	7,11	
13		**Area 8**	**13 days**	**Mon 7/13/26**	**Wed 7/29/26**		
14		Milling (33,613 SY)	4 days	Mon 7/13/26	Thu 7/16/26	9	
15		Patching	1 day	Thu 7/16/26	Thu 7/16/26	14FS-1 day	
16		Paving (3,079 Tons)	4 days	Fri 7/17/26	Wed 7/22/26	11,14,15	
17		Install Speed Humps	2 days	Thu 7/23/26	Fri 7/24/26	16	
18		Install Pavement Markings	3 days	Mon 7/27/26	Wed 7/29/26	12,17	
19		**Area 9**	**11 days**	**Fri 7/17/26**	**Fri 7/31/26**		
20		Milling (48,101 SY)	5 days	Fri 7/17/26	Thu 7/23/26	14	
21		Patching	1 day	Thu 7/23/26	Thu 7/23/26	20FS-1 day	
22		Paving (4,380 Tons)	4 days	Fri 7/24/26	Wed 7/29/26	16,20,21	
23		Install Pavement Markings	2 days	Thu 7/30/26	Fri 7/31/26	18,22	
24		**Alternate 1**	**11 days**	**Fri 7/24/26**	**Fri 8/7/26**		
25		Milling (25,847)	3 days	Fri 7/24/26	Tue 7/28/26	20	
26		Patching	1 day	Wed 7/29/26	Wed 7/29/26	25	
27		Paving (2,208 Tons)	3 days	Thu 7/30/26	Mon 8/3/26	22,25,26	
28		Install Speed Humps	2 days	Tue 8/4/26	Wed 8/5/26	27	
29		Install Pavement Markings	2 days	Thu 8/6/26	Fri 8/7/26	23,28	
30		**Alternate 2 Quebec St.**	**10 days**	**Wed 7/29/26**	**Tue 8/11/26**		
31		Milling (18,080)	2 days	Wed 7/29/26	Thu 7/30/26	25	
32		Patching	1 day	Thu 7/30/26	Thu 7/30/26	31FS-1 day	
33		Paving (2,059 Tons)	2 days	Tue 8/4/26	Wed 8/5/26	31,27	
34		Install Speed Humps	2 days	Thu 8/6/26	Fri 8/7/26	33	
35		Install Pavement Markings	2 days	Mon 8/10/26	Tue 8/11/26	34	
36		**Area 2**	**7 days**	**Fri 7/31/26**	**Mon 8/10/26**		
37		Milling (10,348 SY)	1 day	Fri 7/31/26	Fri 7/31/26	31	
38		Patching	1 day	Mon 8/3/26	Mon 8/3/26	37	
39		Paving (880 Tons)	1 day	Thu 8/6/26	Thu 8/6/26	37,38,33	
40		Install Pavement Markings	2 days	Fri 8/7/26	Mon 8/10/26	39	
41		**Area 4**	**7 days**	**Mon 8/3/26**	**Tue 8/11/26**		
42		Milling (5,646 SY)	1 day	Mon 8/3/26	Mon 8/3/26	37	
43		Patching	1 day	Tue 8/4/26	Tue 8/4/26	42	
44		Paving (480)	1 day	Fri 8/7/26	Fri 8/7/26	43,39	
45		Install Pavement Markings	1 day	Tue 8/11/26	Tue 8/11/26	44,40	
46		**Area 5**	**7 days**	**Tue 8/4/26**	**Wed 8/12/26**		
47		Milling (15,867 SY)	2 days	Tue 8/4/26	Wed 8/5/26	42	
48		Patching	1 day	Wed 8/5/26	Wed 8/5/26	47FS-1 day	
49		Paving (1,799 Tons)	2 days	Mon 8/10/26	Tue 8/11/26	47,48,44	
50		Install Pavement Markings	1 day	Wed 8/12/26	Wed 8/12/26	49	
51		**Area 6**	**8 days**	**Thu 8/6/26**	**Mon 8/17/26**		
52		Milling (13,440 SY)	2 days	Thu 8/6/26	Fri 8/7/26	47	
53		Patching	1 day	Fri 8/7/26	Fri 8/7/26	52FS-1 day	
54		Paving (1,524 Tons)	2 days	Wed 8/12/26	Thu 8/13/26	49,52,53	
55		Install Pavement Markings	2 days	Fri 8/14/26	Mon 8/17/26	50,54	
56		**Area 7**	**6 days**	**Mon 8/10/26**	**Mon 8/17/26**		
57		Milling (22,002 SY)	2 days	Mon 8/10/26	Tue 8/11/26	52	
58		Patching	1 day	Tue 8/11/26	Tue 8/11/26	57FS-1 day	
59		Paving	2 days	Fri 8/14/26	Mon 8/17/26	54,57,58	
60		**Area 10**	**7 days**	**Wed 8/12/26**	**Thu 8/20/26**		
61		Milling (11,252 SY)	2 days	Wed 8/12/26	Thu 8/13/26	57	
62		Patchng	1 day	Thu 8/13/26	Thu 8/13/26	61FS-1 day	
63		Paving (1,238 Tons)	2 days	Tue 8/18/26	Wed 8/19/26	61,62,59	
64		Install Pavement Markings	1 day	Thu 8/20/26	Thu 8/20/26	63	
65		**Area 11**	**7 days**	**Fri 8/14/26**	**Mon 8/24/26**		
66		Milling (8,143 SY)	1 day	Fri 8/14/26	Fri 8/14/26	61	
67		Patching	1 day	Mon 8/17/26	Mon 8/17/26	66	
68		Paving (923 Tons)	1 day	Thu 8/20/26	Thu 8/20/26	63,66,67	
69		Install Pavement Markings	2 days	Fri 8/21/26	Mon 8/24/26	64,68	
70		**Area 12**	**9 days**	**Mon 8/17/26**	**Thu 8/27/26**		
71		Milling (22,083 SY)	3 days	Mon 8/17/26	Wed 8/19/26	66	
72		Patching	1 day	Wed 8/19/26	Wed 8/19/26	71FS-1 day	
73		Paving (2,504 Tons)	3 days	Fri 8/21/26	Tue 8/25/26	68,71,72	
74		Install Pavement Markings	2 days	Wed 8/26/26	Thu 8/27/26	69,73	
75		**Area 13**	**10 days**	**Thu 8/20/26**	**Wed 9/2/26**		
76		Milling (31,902 SY)	4 days	Thu 8/20/26	Tue 8/25/26	71	
77		Patching	1 day	Tue 8/25/26	Tue 8/25/26	76FS-1 day	
78		Paving (3,583 Tons)	4 days	Wed 8/26/26	Mon 8/31/26	73,76,77	
79		Install Pavement Markings	2 days	Tue 9/1/26	Wed 9/2/26	74,78	

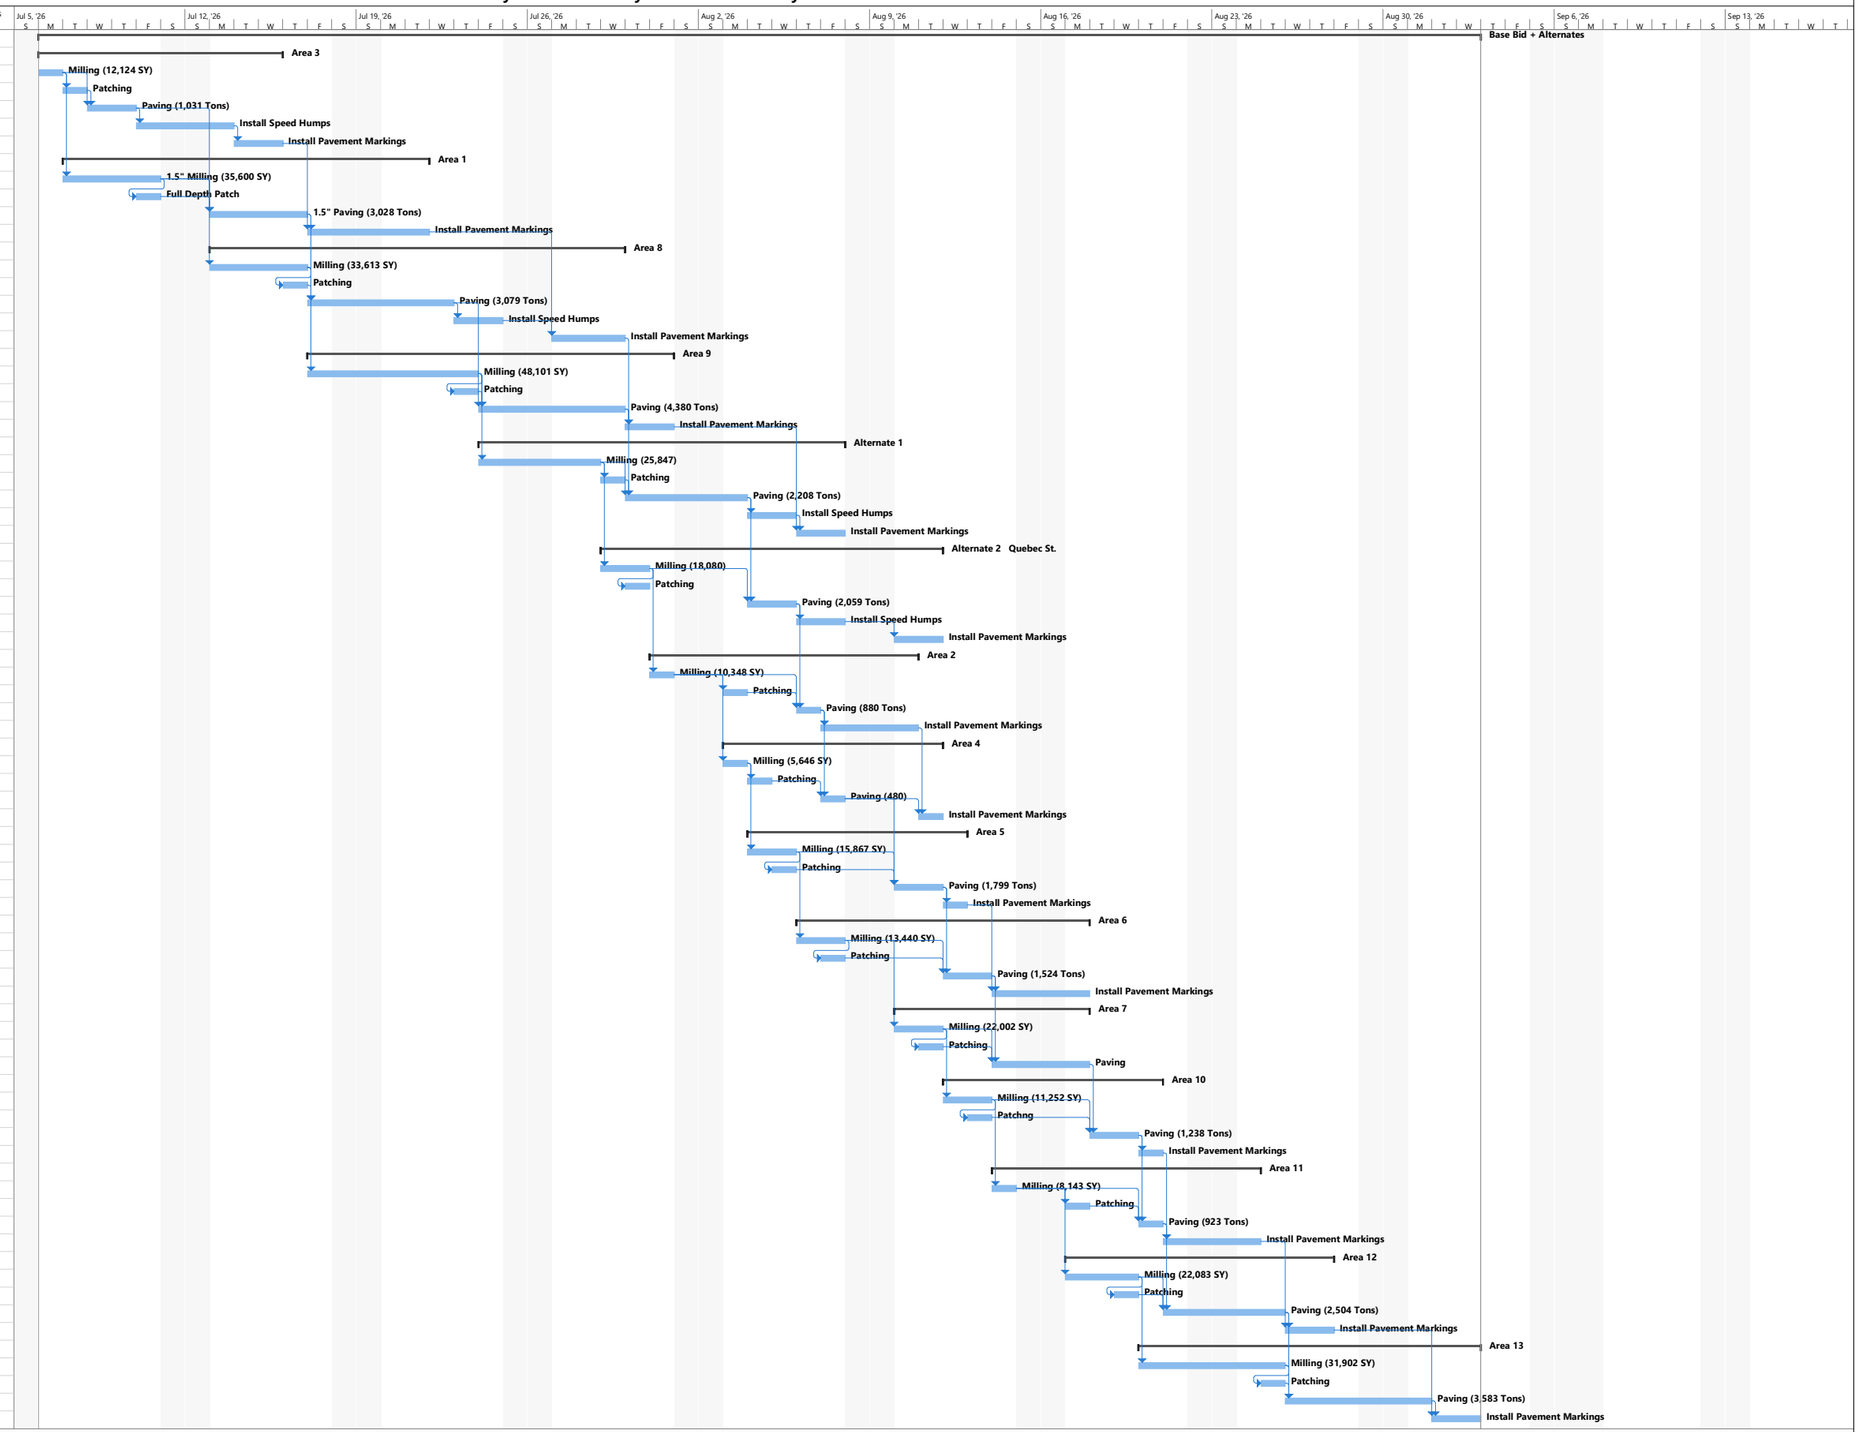

Project: City of Commerce City
Date: Mon 6/29/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
